

Double Distant Signal


CGL - VM

Created by : SSE/SIG/SW/MAS

Project start: **Wed, 10-9-2024**

Display week: **1**

TASK	Unit	ASSIGN	REQUIRED	COMPET	PROGRESS	START	END
CGL - OV Section							
Vegetation Cleaning	Mtrs	Batch 1	5000	4500	90%	10-9-24	11-15-24
Trenching	Mtrs	Batch 1	3000	2000	67%	10-9-24	11-15-24
Horizontal Boring	Mtrs	Batch 1	2000	600	30%	10-9-24	11-15-24
Track Crossing	Nos	Batch 1	4	0	0%	10-9-24	11-15-24
Road Crossing	Nos	Batch 1	1	0	0%	10-9-24	11-15-24
Cable Laying	Mtrs	Batch 1	13600	1000	7%	10-9-24	11-15-24
Provision of GI Pipe	Mtrs	Batch 1	500	0	0%	10-9-24	11-15-24
Location Foundation	Nos	Batch 1	6	0	0%	10-9-24	11-15-24
Signal Foundation	Nos	Batch 1	4	0	0%	10-9-24	11-15-24
Signal Erection	Nos	Batch 1	4	0	0%	10-9-24	11-15-24
Location Wiring	Nos	Batch 1	6	0	0%	10-9-24	11-15-24
Cable Termination	Nos	Batch 1	6	0	0%	10-9-24	11-15-24
Indoor Wiring	Nos	Batch 1	2	0	0%	10-9-24	11-15-24
FAT & SAT	Nos	Batch 1	1	0	0%	10-9-24	11-15-24
Testing and Commissi	Nos	Batch 1	2	0	0%	10-9-24	11-15-24
OV - KGZ Section							
Vegetation Cleaning	Mtrs	Batch 2	5000	1000	20%	11-6-24	11-30-24
Trenching	Mtrs	Batch 2	4000		0%	11-6-24	11-30-24
Horizontal Boring	Mtrs	Batch 2	1000		0%	11-6-24	11-30-24
Track Crossing	Nos	Batch 2	3		0%	11-6-24	11-30-24
Road Crossing	Nos	Batch 2	2		0%	11-6-24	11-30-24
Cable Laying	Mtrs	Batch 2	12000		0%	11-6-24	11-30-24
Provision of GI Pipe	Mtrs	Batch 2	500		0%	11-6-24	11-30-24
Location Foundation	Nos	Batch 2	8		0%	11-6-24	11-30-24
Signal Foundation	Nos	Batch 2	6		0%	11-6-24	11-30-24
Signal Erection	Nos	Batch 2	6		0%	11-6-24	11-30-24
Location Wiring	Nos	Batch 2	8		0%	11-6-24	11-30-24
Cable Termination	Nos	Batch 2	8		0%	11-6-24	11-30-24
Indoor Wiring	Nos	Batch 2	3		0%	11-6-24	11-30-24
FAT & SAT	Nos	Batch 2	1		0%	11-6-24	11-30-24
Testing and Commissi	Nos	Batch 2	3		0%	11-6-24	11-30-24
KGZ - MMK SECTION							
Vegetation Cleaning	Mtrs	Batch 2	5000	0	0%	11-6-24	12-31-24
Trenching	Mtrs	Batch 2	5000		0%	11-6-24	12-31-24
Horizontal Boring	Mtrs	Batch 2	1		0%	11-6-24	12-31-24
Track Crossing	Nos	Batch 2	4		0%	11-6-24	12-31-24
Road Crossing	Nos	Batch 2	1		0%	11-6-24	12-31-24
Cable Laying	Mtrs	Batch 2	1		0%	11-6-24	12-31-24

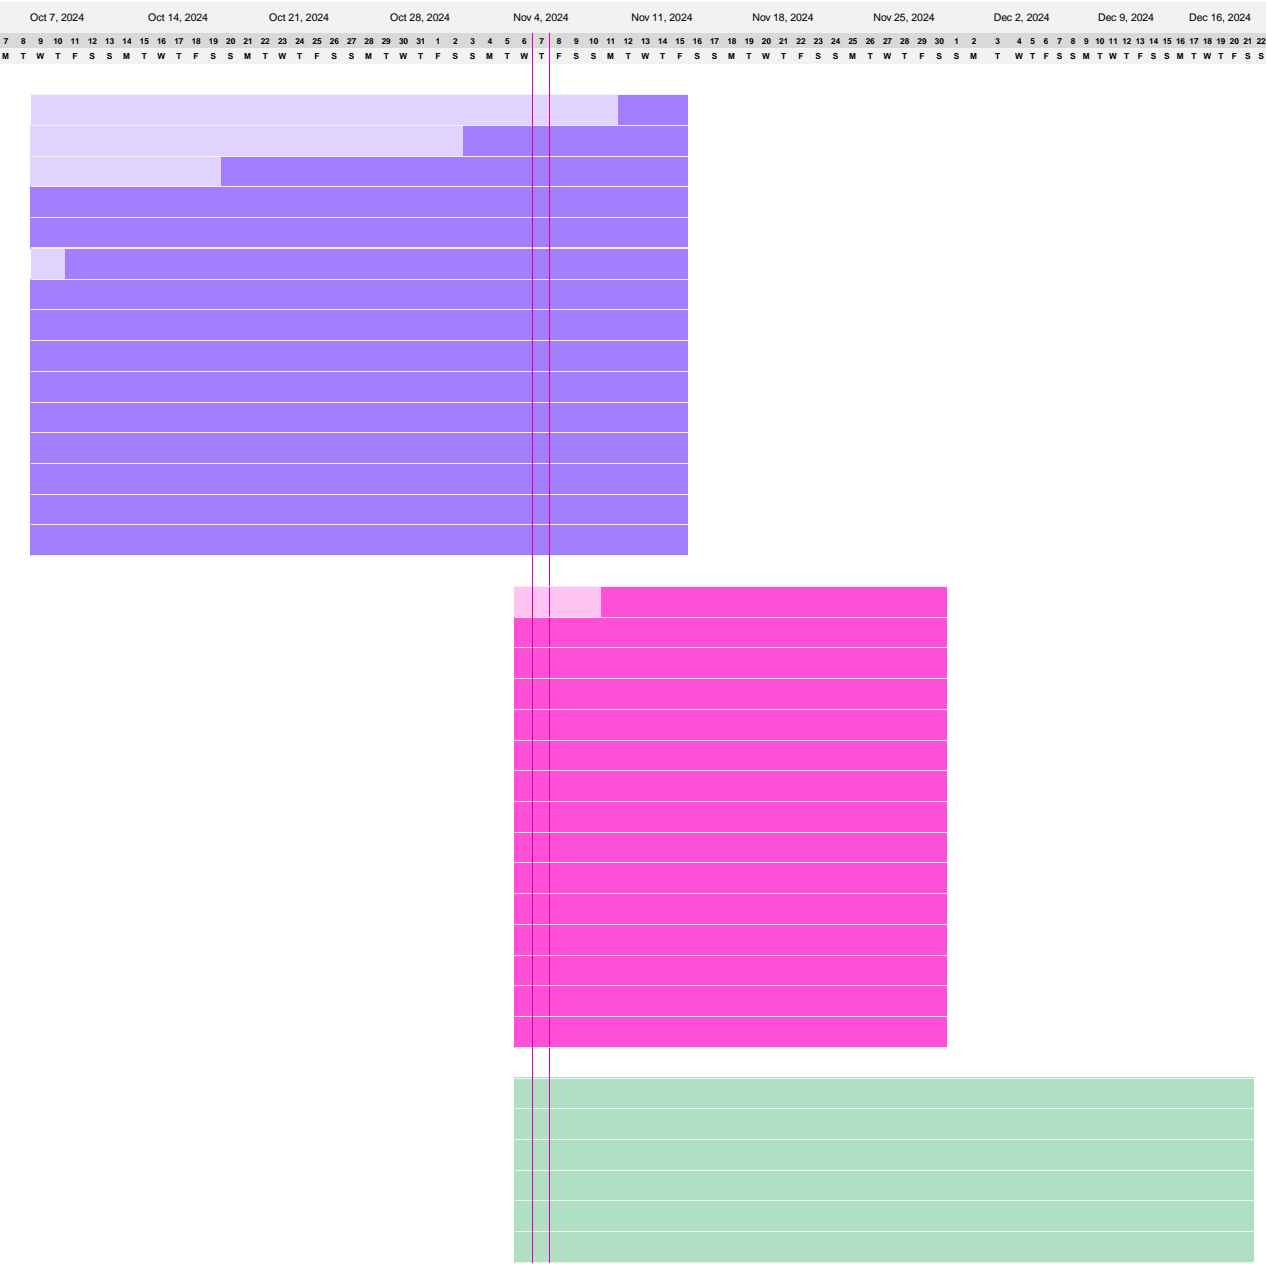

Insert new rows ABOVE this one
